White board
Learning management systems

Name
Razan Alshahrani
Team member 1
Team member 2
Team member 3
Team member 4
Team member 5

List of tables

Table1 project charter 6
Table2 scope statement 8-9
Table3 WBS Dictionary 11
Table4 RACI matrix 12
Table5 Risk register 13

List of Figure

Figure1 WBS 10
Figure2 Gentt chart 12
Figure3 Risk matrix 13

Introduction

In many academic institutions, existing digital platforms have played a central role in supporting online and blended learning. These systems typically offer access to course materials, assignments, announcements, and communication tools that facilitate interaction between students and instructors. Despite their widespread adoption, several persistent challenges remain, most notably, the delay in delivering critical notifications to students.

Students often receive alerts about new assignments, exams, or instructor messages after key deadlines have passed. This delay disrupts academic planning, reduces student responsiveness, and can negatively impact performance. In fast-paced academic environments, timely access to information is essential for managing workload, meeting deadlines, and maintaining engagement.

To address these limitations, this project introduces a standalone academic notification system that operates independently from existing platforms. The system is designed to solve the same core problems—such as delayed alerts and lack of customization—while offering enhanced solutions. It delivers real-time push notifications when new assignments or exams are posted and when grades are released. Notifications are personalized based on user roles (students, instructors, administrators) and academic calendars, ensuring relevance and timeliness Beyond solving known issues, the system introduces additional improvements. These include multi-channel delivery (mobile, email, dashboard), intelligent scheduling, and role-based customization. The system does not replicate or integrate with existing platforms, but instead reimagines the notification experience with a student-centered Approach.

Ultimately, this project reflects a strategic commitment to improving the quality of digital education. By ensuring that academic alerts are timely, relevant, and accessible, the system empowers students to stay informed and proactive, while supporting instructors and administrators in streamlining communication and reducing missed deadlines [1].

Problem statement

- Traditional education systems faced major challenges such as limited difficulties in submitting and communication between instructors and students and limited access to, lack of centralized course management, tracking assignments learning materials outside the classroom [2].

- E-learning and learning management systems (LMSs) were developed to address these challenges by providing digital environments that allow interaction, online assessments, and easy access to educational content [2].

- However, despite their success in improving digital learning, many existing e-learning systems still face technical and usability issues that affect efficiency, engagement, and overall user experience[3].

- Common issues in current LMSs include:

- Delayed notifications, where alerts and updates are not delivered instantly, leading to missed announcements or deadlines [4].
- Slow system performance during high-demand periods, such as examinations or assignment submissions [3].
- Synchronization problems between web and mobile versions, causing inconsistent or missing data [4].
- Outdated or complex user interfaces that reduce accessibility and make navigation difficult [3]
- Limited feedback and progress tracking tools for both students and instructors [3].

- These limitations negatively impact communication, engagement, and satisfaction among users [3].

- Therefore, this project proposes the development of an independent e-learning system designed to overcome these issues by introducing advanced improvements, including:
- A real-time push notification system that ensures immediate delivery of updates and reminders [4].
- A multi-channel notification feature that delivers alerts via email and SMS to guarantee reliability [4].
- Enhanced synchronization between devices and platforms for consistent data flow [4].
- An interactive and user-friendly interface (UI/UX) to simplify navigation and improve usability [3].
- Improved performance and faster system response to support high user activity efficiently [3].

- By addressing these aspects, the proposed system aims to provide a more efficient, engaging, and reliable learning experience for all users [2] [3][4].

Methodology with justification

This project adopts the Incremental Model, which is suitable for systems that require gradual development and improvement. Since the main objective is to enhance the Blackboard Learning Management System (LMS) by resolving the delay in notifications, this model allows the system to be built and delivered in smaller functional parts known as increments. Each increment adds new functionality, ensuring that improvements are introduced step by step and tested before full deployment.

Stages of the Incremental Model:

1. Requirements Gathering:

Collect feedback from students and instructors to identify the root causes of delayed notifications and determine user expectations for faster updates.

2. System Analysis:

Examine technical factors such as synchronization issues and data flow between the Blackboard server and the mobile application to understand the source of delays.

3. Design Phase:

Plan and design the architecture of an enhanced notification system that supports real time message delivery and multi-channel alerts.

4. Implementation (in Increments):

- Increment 1: Develop and integrate an improved in-app notification system to reduce internal delivery delays.

- Increment 2: Introduce external push notifications via email and SMS for broader accessibility.

- Increment 3: Conduct user testing and refine the system based on collected feedback.

5. Testing Phase:

Test each increment individually to verify functionality, reliability, and notification delivery speed before moving to the next phase.

6. Evaluation Phase:

Evaluate the complete system performance after all increments are integrated, focusing on overall efficiency, response time, and user satisfaction.

Reasons for Using the Incremental Model

- Continuous Delivery: Each increment delivers a usable feature, allowing early testing and evaluation.
- Flexibility: Enhancements or adjustments can be added in later increments without redesigning the entire system.
- Risk Reduction: Frequent testing after each increment minimizes the risk of systemwide failures.
- User Involvement: Students and instructors can interact with each version and share feedback to guide subsequent development.

- Efficient Resource Use: Developers can concentrate on one component at a time, ensuring higher quality and maintainable progress.

Comparison with Other Models

Unlike the Waterfall model, which requires completing all phases before producing a functional version, the Incremental model supports partial delivery and progressive improvement. It is also more structured and predictable than Agile/Scrum, making it ideal for projects like this one — where the focus is on steady enhancement and reliability testing rather than rapid iteration

project charter

TABLE 4-1

Project Title: Intelligent Academic Notification System

Date of Authorization: October 1, 2025

Project Start Date: October 1, 2025 **Projected Finish Date:** December 5, 2025

Key Schedule Milestones:

- Complete requirement analysis and design by October 20
- Go-live with the improved notification system by December 5
- Implement and test the improved notification system November 25

Budget Information: The university has set aside $50,000 for this initiative. Additional funds can be accessed if requi red. The budget will primarily finance software creation, testing instru ments, and cloud notification services

Project Manager: Saba, Project Manager Contact: saba@pnu.edu.sa

Project Objectives:
1-Enhance the academic platform by providing accurate and timely notifications for key academic events
2-Allow students, instructors, and administrators to customize their notification preferences according to their roles
3-Support multiple notification channels such as email, mobile alerts, and in-system messages to enhance communication
4-Automatically send notifications based on scheduled academic data and calendar updates, without needing real-time synchronization
5-Ensure the notification system operates securely, reliably, and independently from existing academic platforms
6-Improve system speed to guarantee fast delivery of notifications, even during busy academic periods
7-Enable high concurrency to process many notifications simultaneously without delays, conflicts, or duplicates

Main Project Success Criteria:
-Notifications are delivered promptly and precisely to each user through their chosen method, such as email, mobile, or dashboard
-Users have the ability to configure their preferences and access their notification records.
-The system operates safely and autonomously, utilizing scheduled data feeds.
-Users are 90% pleased with the system's efficiency and dependability.

Approach:

- Carry out surveys among students and faculty to pinpoint existing problems with Blackboard notifications.
- Complete the requirements, scope statement, and detailed schedule within one month
- Create and evaluate new functionalities (real-time push notifications, customizable settings)
- Conduct weekly meetings to review progress with the sponsor and team.
- Conduct comprehensive system testing and initial deployment prior to the complete launch

ROLES AND RESPONSIBILITIES

Name	Role	Position	Contact Information
Saba	Project Manager	Team Member.	saba@pnu.edu.sa
Yara	Developer	Team Member	yara@pnu.edu.sa
Razan	Designer	Team Member	razan@pnu.edu.sa
Budur	programmer	Team Member	Budur@pnu.edu.sa
Aryam	programmer	Team Member	aryam@pnu.edu.sa
Thekra	programmer	Team Member	thekra@pnu.edu.sa

Sign-off: (Signatures of all the above stakeholders)

Saba Budur

Yara Aryam

Razan Thekra

Comments: (Handwritten or typed comments from above stakeholders, if applicable)

"I am excited to lead this project as a student manager. Improving Blackboard notifications will help students stay more engaged and organized." – Saba

"I'm excited to be part of this project and look forward to helping develop a notification system that truly supports students in keeping up with their tasks and academic deadlines."
— Razan

Table 1 project charter

Techniques for collecting requirements

1.Stakeholders: Instructors, Academic Administrators
- **Technique: Interviews**
- **Reason:**

Interviews offer in-depth understanding of academic workflows, notification policies, and approval procedures. They assist in revealing concealed requirements and elucidating regulations that directly affect the system.

2.Stakeholders: Students
- **Technique: Questionnaires / Surveys**
- **Reason:**

Surveys effectively collect extensive feedback from students about their preferences for notifications and the issues they face with existing systems. This aids in making knowledgeable choices regarding design and usability.

3.Stakeholders: IT Support Staff, Project Team
- **Technique: Focus Groups**
- **Reason:**

Focus groups promote cooperative dialogue among technical personnel and project participants. They assist in pinpointing system issues, improving technical specifications, and confirming the practicality of suggested functionalities.

Project Requirements

Software Requirements
- Reliable authentication and access control based on roles for students, teachers, and administrators.
- Event notification system designed to handle academic occurrences and automatically produce alerts.
- A delivery system that utilizes multiple channels, including email, push notifications, and alerts within the dashboard.

Hardware Requirements
- A web server to support the independent notification system
- A database server for storing user information, school calendars, and alert records.
- Network resources adequate to manage peak demands during academic due dates

Functional Requirements
- Students should get prompt alerts via their chosen methods (email, dashboard alerts)
- The system should enable users to personalize notification settings and choose to optin or opt-out of particular categories.
- The system should automatically activate alerts according to established academic guidelines.
- The system needs to distinctly differentiate permissions among students, instructors, and administrators

Non-functional Requirements
- Scalability: capacity to allocate resources during peak traffic times without compromising performance
- Performance: excellent responsiveness with minimal downtime and rapid data processing
- Security: robust security measures to safeguard user information and adhere to applicable regulations
- Reliability: elevated accessibility and reduced downtime through a sturdy failover management and data recovery system
- Speed: The system needs to provide notifications within seconds of receiving academic events, guaranteeing quick processing and low delay during high activity times
- Concurrency: The system should be capable of managing numerous notification events at the same time, enabling effective processing even during busy acad emic periods without issues, delays, or repetitions

Scope Statement

PROJECT SCOPE STATEMENT

Project title: white board learning management system Date Prepared: October 1, 2025

Project Scope Description:

This project aims to develop a standalone academic notification system that intelligently manages and delivers alerts related to students' academic activities. The system addresses limitations observed in existing platforms by introducing enhanced notification mechanisms. Key features .include automatic alerts when new assignments or exams are posted, and when grades are released Notifications are personalized based on user roles and academic schedules. Although the system is not affiliated with any existing academic platform, its design is informed by the challenges and gaps .identified in current systems, and it offers improved solutions independently

Project Deliverables:

- A standalone web-based academic notification system
- Intelligent scheduling engine based on academic calendars and user roles
- Automatic notifications for:
- New assignments or exams posted
- Grade releases for assignments and tests
- Multi-channel delivery: mobile push, email, and dashboard alerts
- Role-based customization for students, instructors, and admins
- Administrative dashboard for managing notification rules and logs
- User interface for managing preferences and viewing notification history
- Technical documentation and training materials

Product acceptance criteria:

- Notifications must be delivered accurately and in a timely manner
- The system must support role-based customization for different user types
- Users must be able to view, manage, and archive their notification history
- The system must operate independently and securely
- All features must comply with institutional privacy and data protection standards

Project exclusions:

- The system does not perform grading, assignment submission, or content delivery itself, but it sends notifications when such events occur (e.g., grade release, new assignment posted)
- The system does not synchronize in real time with institutional databases, but relies on scheduled or manual data inputs to trigger notifications
- It will not replicate or mention the name of any existing academic platform, but will address the same problems and offer improved solutions independently

Page 1 of 2

PROJECT SCOPE STATEMENT

Project constraints

- Limited access to institutional academic systems and databases
- Project schedule limitations and fixed deadlines
- Data privacy and compliance requirements
- Potential integration challenges with third-party systems

Project assumptions

- Academic calendars and schedules will be made available to configure the notification engine
- Users (students, instructors, admins) will have access to mobile devices or email to receive notifications
- Feedback from users of current systems will be used to identify gaps and refine features
- The system will be hosted independently and maintained without dependency on institutional infrastructure

Table 2 scope statement

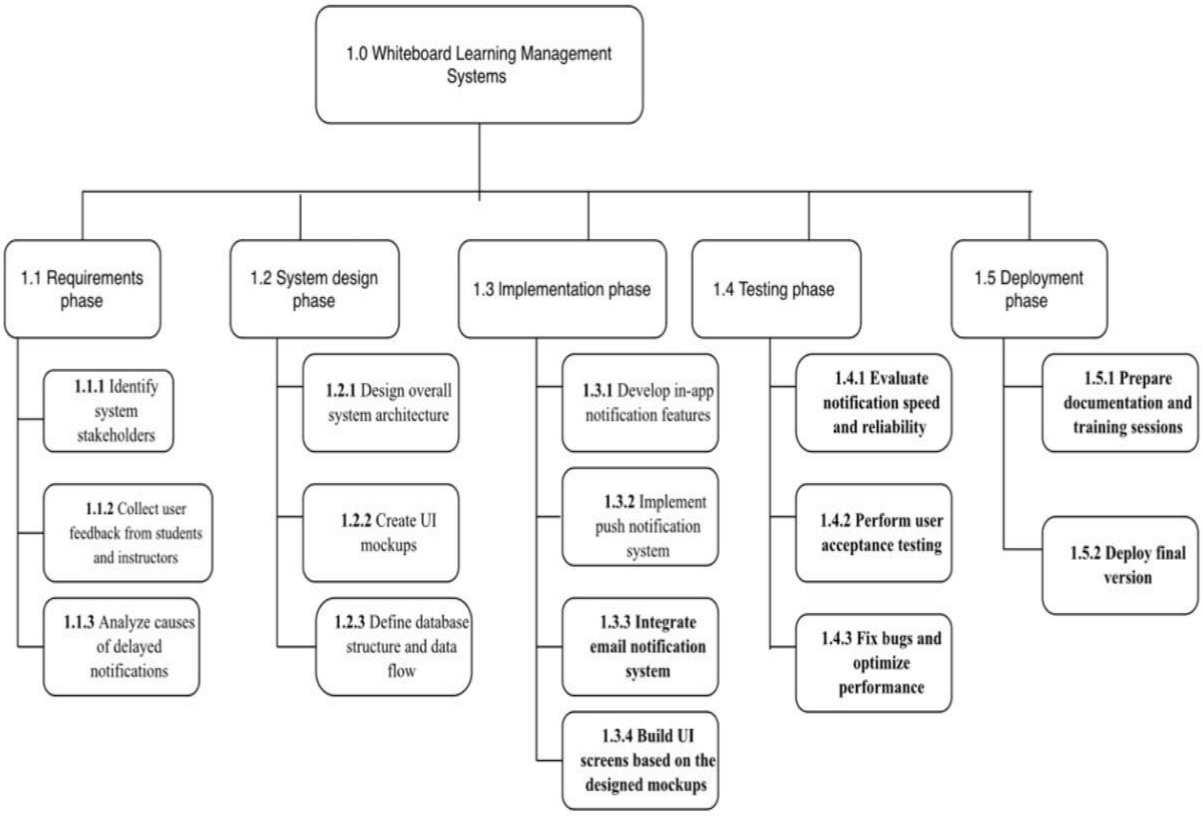


Figure 1 WBS whiteboard learning management systems project

WBS

This figure shows the main phases and tasks of the Whiteboard Learning Management System project. It breaks down the work into five phases: Requirements, Design, Implementation, Testing, and Deployment. Each phase includes specific tasks with IDs to help organize and manage the project more clearly.

WBS Dictionary- Whiteboard Learning Management Systems

Task ID	Task Name	Description	Responsible Person	Estimated Duration
1.1.1	Identify system stakeholders	List and confirm key project stakeholders	Project Manager (PM)	1 day
1.1.2	Collect user feedback	Collect user feedback from students and instructors through surveys and interviews	Business Analyst (BA)	2 days
1.1.3	Analyze causes of delayed notifications	Identify root causes behind delayed notifications	System Analyst	2 days
1.2.1	Design overall system architecture	Design the overall system architecture including modules, interfaces, and integration points	System Architect	3 days
1.2.2	Create UI mockups	Create UI prototypes for notification flow	UI/UX Designer	2 days
1.2.3	Define database structure and data flow	Define database schema and data flow	Database Engineer	3 days
1.3.1	Develop in-app notification features	Implement inside-app notification functionality	Frontend Developer	4 days
1.3.2	Implement push notification system	Integrate push notification service	Backend Developer	4 days
1.3.3	Integrate email notification system	Develop email alert integration	Backend Developer	3 days
1.3.4	Build UI screens	Build UI screens based on the designed mockups	Full-stack Developer	4 days
1.4.1	Evaluate notification speed and reliability	Test realtime delivery performance	Tester	3 days
1.4.2	Perform user acceptance testing	Conduct UAT with students and instructors	QA Team	2 days
1.4.3	Fix bugs and optimize performance	Resolve issues and enhance system performance	Developer	2 days
1.5.1	Prepare documentation and training sessions	Create user guides and conduct training	PM / Trainer	1 days
1.5.2	Deploy final version	Launch final version to production environment	DevOps Engineer	1 days

Table3 WBS Dictionary - Whiteboard Learning Management Systems

WBS dictionary

This table presents the Work Breakdown Structure (WBS) Dictionary for the project. It outlines notification system tasks, including task IDs, names, descriptions, responsible roles, and estimated durations, providing a structured reference for project management and tracking.

RACI chart

	PM	BA	System Analyst	System Architect	UI/UX	DB Engineer	Frontend Dev	Backend Dev	Full-Stack Dev	QA/Tester	DevOps
Identify system stakeholders	R A	C	I	I	I	I	I	I	I	I	I
Collect user feedback	A	R	C	I	I	I	I	I	I	I	I
Analyze causes of delayed notifications	A	C	R	C	I	C	I	I	I	I	I
Design overall system architecture	A	I	C	R	I	C	I	I	I	I	I
Create UI mockups	A	I	I	I	R	I	C	C	C	I	I
Define database structure & data flow	A	I	C	C	I	R	I	I	I	I	I
Develop in-app notification features	A	I	I	I	C	I	R	I	I	I	I
Implement push notification system	A	I	I	I	I	I	I	R	I	I	I
Integrate email notification system	A	I	I	I	I	I	I	R	I	I	I
Build UI screens	A	I	I	I	C	I	C	C	R	I	I
Evaluate notification speed & reliability	A	I	C	I	I	I	I	I	I	R	I
Perform user acceptance testing	A	C	I	I	I	I	I	I	I	R	I
Fix bugs and optimize performance	A	I	I	I	I	I	C	C	R	R	I
Prepare documentation & training	R A	I	I	I	I	I	I	I	I	I	I
Deploy final version	A	I	I	I	I	I	I	I	I	I	R

Table4 RACI matrix assigned to each project task

Gantt chart

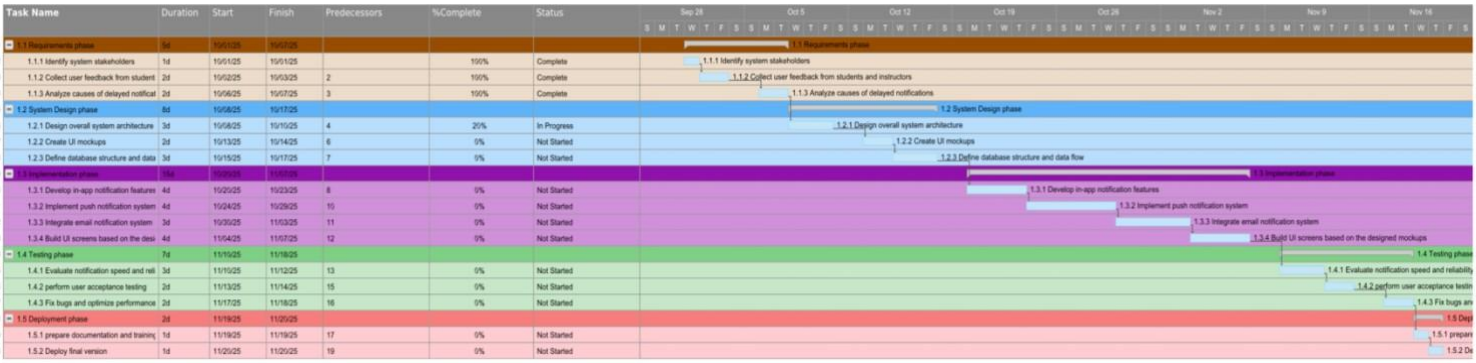


Figure2 Gantt chart for the Intelligent Academic Notification system project

Figure 3 presents the Gantt chart for the Intelligent Academic Notification System Project. The chart illustrates the main project phases: requirements gathering, system design, implementation, testing, and final deployment. It also shows the sequence of tasks, their dependencies, and the completion percentage for each activity. This visual representation helps track project progress and understand how tasks flow together until the final system release.

Milestones:

1. Requirements Phase Completed (End of identifying all project requirements)

2. System Design Approved (Architecture and UI/UX design finalized)

3. Development Phase Completed (Core system features implemented)

4. Testing Phase Completed (System successfully tested and validated)

5. Final Project Completed & Submitted (All deliverables done and project officially closed)

Risk register

ID	Category	Risk description	Cause	Trigger	Type (Threat/Opportunity)	Probability (1-5)	Impact (1-5)	Score (P×I)	Response strategy	Planned actions	Owner	Due date	Status	Residual risk	Contingency plan
1	Schedule	Delay in completing increment due to overlapping tasks	Poor time estimation and task overlap	Sprint tasks spill into next increment	Threat	3	4	12	Mitigate	Refine sprint backlog, allocate buffer days between increments	Project Manager	2025-11-20	Open	Medium	Reassign developer or adjust next increment timeline
2	Requirement	New request from academic staff mid-project	Late feedback from stakeholders	New feature requested after increment delivery	Threat	3	5	15	Avoid	Freeze requirements after initial increment; create change request form	Business Analyst	2025-11-18	Open	Low	Defer new requests to later release cycle
3	Technical	Integration with Blackboard notification API fails intermittently	API limitations or downtime	API response errors or timeouts	Threat	2	5	10	Transfer	Use cached notifications and alert user; contact IT for SLA	Tech Lead	2025-11-15	Open	Low	Fallback to manual sync via CSV export
4	Quality	Bug in notification filter affects accuracy	Insufficient testing in earlier increments	Incorrect notifications displayed	Threat	3	4	12	Mitigate	Add regression tests; peer review code before merge	QA Lead	2025-11-22	In progress	Low	Rollback to previous version if critical
5	Resources	Limited availability of tester during finals week	Tester exam schedule	Testing phase postponed	Threat	3	3	9	Mitigate	Cross-train another member for testing tasks	Project Manager	2025-11-25	Open	Medium	Borrow resource from dev team temporarily
6	Opportunity	University's tech expo aligns with release date	Event timing	Event announcement	Opportunity	3	4	12	Exploit	Prepare demo and marketing material for exposure	PM & Marketing	2025-11-30	Planned	Low	Submit demo registration early
7	Security	User data not encrypted properly in local storage	Improper handling of credentials	Security review findings	Threat	2	5	10	Mitigate	Encrypt sensitive data; add validation before saving	Security Lead	2025-11-28	In progress	Low	Disable local caching if issue persists
8	Infrastructure	Server capacity insufficient for high user load	Limited hosting plan	Slow response time under load	Threat	2	4	8	Mitigate	Upgrade to scalable hosting or use load balancing	DevOps Engineer	2025-12-01	Open	Low	Move to backup server if downtime >1h
9	Opportunity	Mentor from IT department offers technical guidance	Mentor initiative	Mentor contact email	Opportunity	4	3	12	Enhance	Schedule mentoring sessions to improve code quality	Tech Lead	2025-11-18	Scheduled	Low	Share lessons learned with full team
10	Compliance	App not aligned with university IT policy on notification permissions	Lack of policy review	Policy review meeting	Threat	2	4	8	Mitigate	Review policies and update consent text in app	BA / Legal	2025-11-26	In progress	Low	Disable push notifications until approval

Table5 Risk Register

Risk Level	Score Range	Description	Example Risks
High	15–25	Requires immediate action and mitigation plan	Stakeholder late requests, API instability
Medium	8–12	Needs monitoring and controlled response	Testing delay, notification filter bug
Low	1–7	Acceptable, monitor occasionally	Server load, cost increase

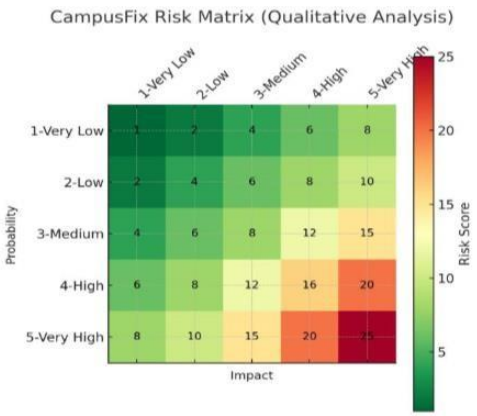


Figure 3 Risk Matrix

References

[1] Blackboard Inc., “Blackboard App Feature Guide,” *Blackboard Help*, [Online]. Available: https://help.blackboard.com/ar-sa/Blackboard_App/Feature_Guide. Accessed: Oct. 22, 2025.

[2] Blackboard Inc., “Learning Management Systems: Overview and Features,” Blackboard Official Website, 2023. [Online]. Available: https://www.blackboard.com

[3] Blackboard Help Center, “Common Issues and Troubleshooting in Blackboard Learn,” Blackboard Support Documentation, 2023. [Online]. Available: https://help.blackboard.com

[4] Blackboard Learn Documentation, “Blackboard Learn Mobile App: Notifications and Settings,” Blackboard User Guide, 2023. [Online]. Available: https://help.blackboard.com/Learn
